

Referendum Project Update

Monthly Update: Period 6/1/2021 – 6/15/2021

PHASE 1 – Gower Middle School

Parking Lot

Tuesday, 6/1/2021, the crew was onsite and beginning to tear up the existing parking lot. The weather has been extremely cooperative so far and the project is right on schedule.

Completed to date:

- Old asphalt removed and prepared for new asphalt
- Removal of damaged/uneven concrete from North entrances
- New concrete curbs installed at SW entrance lot
- South entrance concrete skirt installed
- Drainage piping installed in SW entrance lot

Anticipated Project Completion: 7/1/2021



Waterproofing

On the North side of the building (band room) we have always had water infiltration issues. The company dug 8-10 feet along the building and found 5-6 areas of serious cracks in the building's foundation. These cracks were sealed and then the particular section of the building was wrapped and is now waterproof.

Anticipated Project Completion: 6/14/2021




Classroom Renovation

Classroom renovations are well underway and on schedule so far.

Completed to date:

- Classrooms emptied
- First and second coat of paint
- New carpet flooring has been delivered
- Asbestos abatement
- New whiteboards have been delivered

Anticipated Project Completion: 8/1/2021

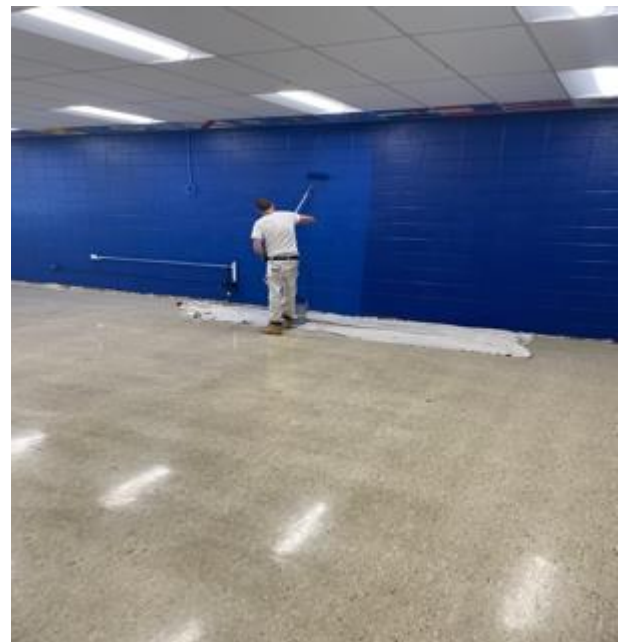



Roof Top Units

Two final roof top units are being installed. This will complete the 3-year RTU replacement plan for Gower Middle School.

Completed to date:

- Old units removed
- New units delivered

Anticipated Project Completion: 6/24/2021

